



DUCT SEALING REPORT


Duct Sealing Performed For:

Micas, Taylor 83 Tranquility mandeville , LA 70448		AEROSEAL CASE ID: 5846 SYSTEM DESCRIPTION: upflow 5 ton unit 2 SEAL DESCRIPTION: Sealing supply and return HARDWARE: HomeSeal Connect TECHNICIAN: Alfred Detillieu
DATE: 11/8/2023		

Overall Sealing Results:

<u>BEFORE</u> SERVICE 346.6 CFM of Leakage , equivalent to a 65.5 Square Inch Hole or 17% of the system capacity of 2000.0 CFM
<u>AFTER</u> SERVICE 25.2 CFM of Leakage , equivalent to a 4.8 Square Inch Hole or 1.3% of system capacity
This corresponds to a 93% Reduction in Duct Leakage
NOTE: Duct leakage results are calculated in Cubic Feet per Minute (CFM) measured at a STANDARD OPERATING PRESSURE of 25 Pa.

Aeroseal Sealing Progress:

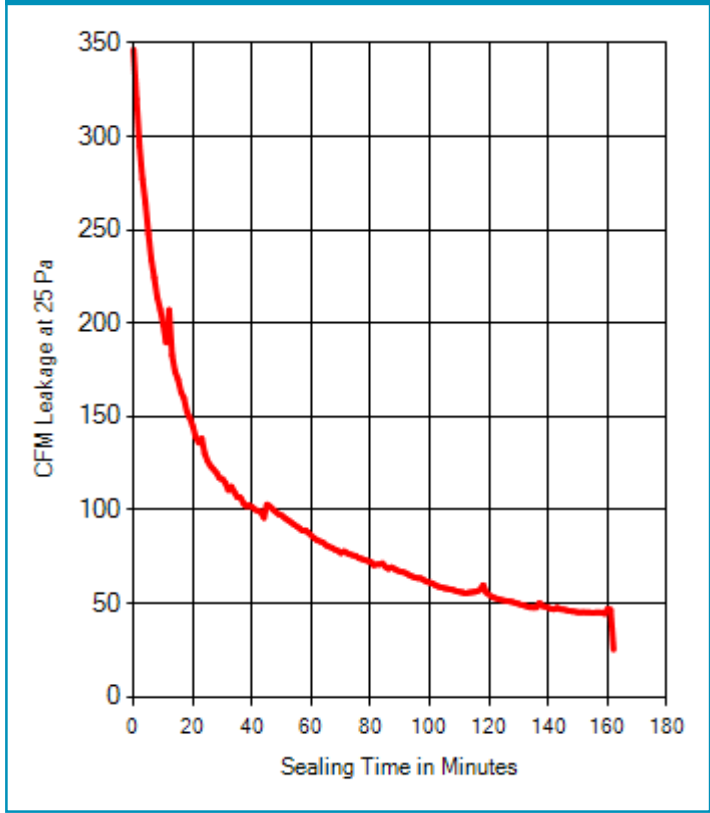

Duct Sealing Performed By:

	Eco Seal, LLC 1329 Albert Street Mandeville, La , La 70448 Phone: 986-789-6076
--	--

Aeroseal process uses DuctSeal sealant that is certified to meet requirements listed in UL 1381 standard- "Outline of investigation for Aerosol Duct Sealant" Please provide Aeroseal feedback at <http://bit.ly/2021aeroseal> and reference code **LPXJXLR**.
